



Addison Airport - Westside Schedule
1999

11

| | | |
|---|-----------------|--|
| Project No. : TXDOT#9842 ADDSN BID#98-4. Addison Airport-West Taxiway Transmittal of shop drawings, monolithic drawings, equipment data, material samples, manufactures certification of compliance, etc., for approval by the engineer. Request for Engineer's review of the following items. To: Wise Contractors-Consultants, Inc. Rt. 1 Box 562 2 Oakwood, TX 75855 | Date: 01-May-98 | <input checked="" type="checkbox"/> Original Submittal <input type="checkbox"/> Re-Submittal <input type="checkbox"/> Urgent Requested Return Date : 10-May-98 H. B. Zachry Submittal #: 107 |
| From: H.B. Zachry Company 16101 Dooley Rd. Addison, TX 75244 | | |

| Description of Item Submitted i.e. Type, Size, Model No., etc. | Manufacturer or Supplier | Mfg. or Cont. Cat., Curve Drawing of Brochure No. | C O P I E S | Project Specification Section Number | Project Drawing Sheet or Plate No. |
|---|-----------------------------|--|----------------------------|---|---|
|  ATTACHED PLEASE FIND 1 Target Schedule/Addison Airport-West Taxiway | H.B. Zachry | | 6 | 100 | |


Signature of Contractor




 Majed Limam, Project Controls Manager

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish | Total Float | PHAS | AREA | 1998 | | | | | | | | | | | | 1999 | | | | | | | | | | | | | | | | | | | | | | | | | | |
|-------------|----------------------|----------|-------------|--------------|-------------|------|------|------|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|----|------|---|---|----|----|----|---|----|----|----|---|----|----|----|----|---|----|----|----|---|----|----|----|---|---|----|----|
| | | | | | | | | MAR | APR | MAY | JUN | JUL | AUG | SEP | OCT | NOV | DEC | JAN | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | | | | | 2 | 9 | 16 | 23 | 30 | 6 | 13 | 20 | 27 | 4 | 11 | 18 | 25 | 1 | 8 | 15 | 22 | 29 | 6 | 13 | 20 | 27 | 3 | 10 | 17 | 24 | 31 | 7 | 14 | 21 | 28 | 5 | 12 | 19 | 26 | 2 | 9 | 16 | 23 |

| 00 PRE-CONSTRUCTION PLANNING | | | | | | |
|-------------------------------------|----------------------------------|----|---------|---------|-------|-------|
| DDZA | Project Preplanning | 21 | 02MAR98 | 16APR98 | 0 00 | DDALL |
| DDZX | Set Up Resident Engineer Trailer | 6 | 17APR98 | 28APR98 | 10 00 | DDALL |
| DDZB | Contractor Mobilization | 10 | 17APR98 | 06MAY98 | 0 00 | DDALL |
| MILE1 | Start Construction | 0 | 06MAY98 | | 0 00 | DDB/F |
| DDAA | PROJECT BARRICADES | 6 | 06MAY98 | 16MAY98 | 0 00 | DDALL |



| 01 PHASE 01 | | | | | | |
|--------------------|--|----|---------|---------|--------|-------|
| DDBA | Erosion Control | 7 | 06MAY98 | 18MAY98 | 103 01 | DDALL |
| DDCA | 42" RCP Excavate, Bed, Lay, & Backfill | 17 | 06MAY98 | 03JUN98 | 29 01 | DDB/F |
| DDAC | Detour Between Driveways 1-2 SOUTH END B/C | 2 | 08MAY98 | 11MAY98 | 2 01 | DDB/C |
| DDBT | Displace Threshold | 1 | 11MAY98 | 11MAY98 | 0 01 | DDB/F |
| DDBJ | Milling T/W B/C | 2 | 12MAY98 | 14MAY98 | 0 01 | DDB/C |
| DDAB | Detour Between Driveways 9-10 | 1 | 15MAY98 | 15MAY98 | 5 01 | DDB/F |
| DDBB | Demo Conc Pav T/W B/F | 2 | 15MAY98 | 18MAY98 | 5 01 | DDB/F |
| DDBD | Milling Phase I B/F | 2 | 15MAY98 | 18MAY98 | 5 01 | DDB/F |
| DDEH | Excavate & Haul T/W B/C | 6 | 15MAY98 | 26MAY98 | 0 01 | DDB/C |
| DDNH | Lime T/W B/C | 6 | 27MAY98 | 03JUN98 | 0 01 | DDB/C |
| DDPH | Electrical Conduits T/W B/C | 6 | 27MAY98 | 03JUN98 | 0 01 | DDB/C |
| DDEA | Excavate & Haul T/W B/F | 7 | 27MAY98 | 04JUN98 | 1 01 | DDB/F |
| DDEB | Knockdown Uncl Excavation @Waste Area | 40 | 27MAY98 | 27JUL98 | 59 01 | DDALL |
| DDNJ | Crushed Aggr. Base Course T/W B/C | 6 | 04JUN98 | 12JUN98 | 0 01 | DDB/C |
| DDCF | 36" RCP Excavate, Bed, Lay, & Backfill | 7 | 04JUN98 | 15JUN98 | 29 01 | DDB/F |
| DDNA | Lime Phase I B/F | 7 | 04JUN98 | 16JUN98 | 1 01 | DDB/F |
| DDLA | ExcFgFPFC/R Inlets & Manholes | 10 | 04JUN98 | 19JUN98 | 39 01 | DDB/F |
| DDPA | Electrical Conduits T/W B/F | 6 | 06JUN98 | 15JUN98 | 1 01 | DDB/F |
| DDQJ | Concrete Paving T/W B/C | 8 | 15JUN98 | 26JUN98 | 0 01 | DDB/C |
| DDCH | 30" RCP Excavate, Bed, Lay, & Backfill | 6 | 16JUN98 | 24JUN98 | 29 01 | DDB/F |
| DDNB | Crushed Aggr. Base Course T/W B/F | 6 | 16JUN98 | 24JUN98 | 1 01 | DDB/F |
| DDQH | LAY TY D SURF T/W C TY "L" JT (1 EA) | 1 | 26JUN98 | 26JUN98 | 33 01 | DDB/C |
| DDTH | REDRESS AFTER CONC PAV T/W B/C | 2 | 26JUN98 | 29JUN98 | 28 01 | DDB/C |
| DDQN | LAY SURF T/W B-ASPH ACCESS(2 EA)south end T/W B/ | 3 | 26JUN98 | 30JUN98 | 25 01 | DDB/C |
| DDQB | Concrete Paving T/W B/F | 28 | 26JUN98 | 06AUG98 | 0 01 | DDB/F |
| DDBTA | Return Threshold | 1 | 30JUN98 | 30JUN98 | 32 01 | |
| DDVH | Electrical Light, Signage, T/W B/C | 6 | 30JUN98 | 08JUL98 | 28 01 | DDB/C |
| DDTA | REDRESS AFTER CONC PAV Ph 1 T/W B/F | 2 | 07AUG98 | 10AUG98 | 0 01 | DDB/F |
| DDUH | Markings T/W B/F & B/C | 1 | 11AUG98 | 11AUG98 | 4 01 | DDB/F |

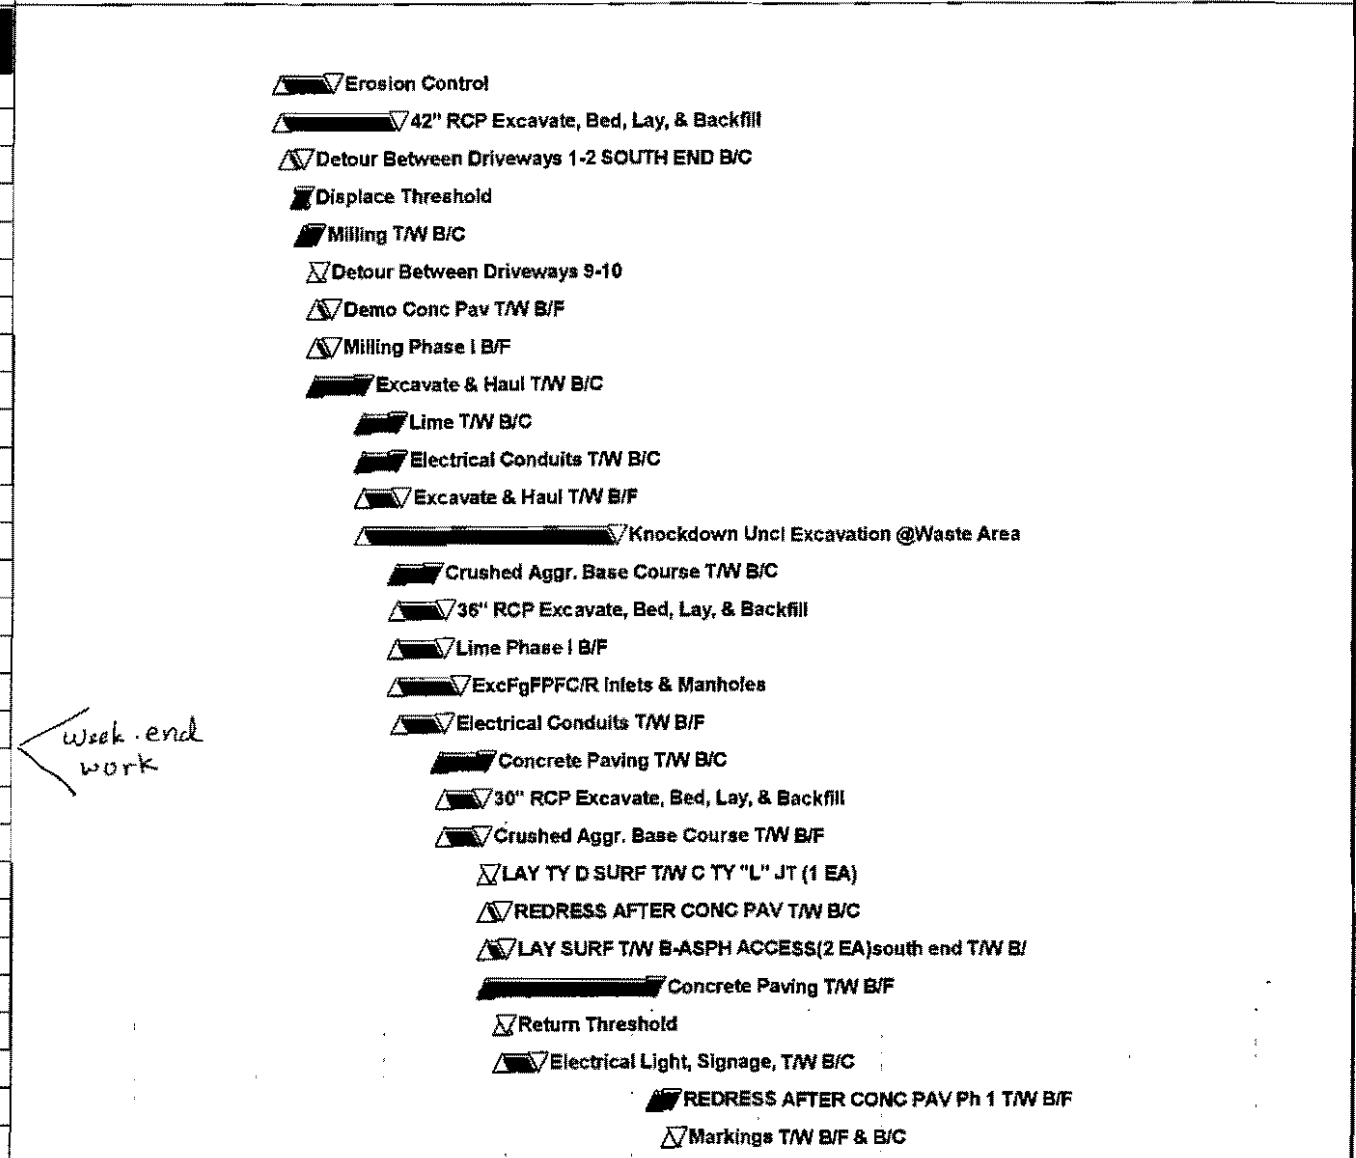

week end work

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish | Total Float | PHAS | AREA | 1998 | | | | | | | | | | | | 1999 | | | | | | | | | | | | | |
|-------------|--------------------------------|----------|-------------|--------------|-------------|------|-------|----------------------------------|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|----|------|---|---|----|----|----|---|----|----|----|---|---|----|----|
| | | | | | | | | MAR | APR | MAY | JUN | JUL | AUG | SEP | OCT | NOV | DEC | JAN | | | | | | | | | | | | | | | |
| | | | | | | | | 2 | 9 | 16 | 23 | 30 | 6 | 13 | 20 | 27 | 4 | 11 | 18 | 25 | 1 | 8 | 15 | 22 | 29 | 5 | 12 | 19 | 26 | 2 | 9 | 16 | 23 |
| DDVA | Elect Lighting Signage T/W B/F | 5 | 11AUG98 | 17AUG98 | 0 01 | | DDB/F | █ Elect Lighting Signage T/W B/F | | | | | | | | | | | | | | | | | | | | | | | | | |
| MILE2 | End of Phase 1 | 0 | | 17AUG98 | 0 01 | | DDB/F | ◆ End of Phase 1 | | | | | | | | | | | | | | | | | | | | | | | | | |

01A PHASE 01A

| | | | | | | | | | | | | | | | | | | | | | | | | | | |
|-------|-----------------|---|---------|---------|--------|--|-------|-------------------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
| DDEC | Week End Work 1 | 2 | 06JUN98 | 07JUN98 | 29 01A | | DDE/F | △ Week End Work 1 | | | | | | | | | | | | | | | | | | |
| DDEC2 | Week End Work 2 | 2 | 13JUN98 | 14JUN98 | 29 01A | | DDE/F | △ Week End Work 2 | | | | | | | | | | | | | | | | | | |

02 PHASE 02

| | | | | | | | | | | | | | | | | | | | | | | | | | | |
|-------|---------------------------------------|----|---------|---------|-------|--|-------|---|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
| MILE3 | Begin Phase 2 | 0 | 18AUG98 | | 0 02 | | DDB/E | ◆ Begin Phase 2 | | | | | | | | | | | | | | | | | | |
| DDBH | Demo Conc Pav B/E Ph 2 | 2 | 18AUG98 | 19AUG98 | 1 02 | | DDB/E | △ Demo Conc Pav B/E Ph 2 | | | | | | | | | | | | | | | | | | |
| DDBG | Milling Phase II B/E | 3 | 18AUG98 | 20AUG98 | 0 02 | | DDB/E | █ Milling Phase II B/E | | | | | | | | | | | | | | | | | | |
| DDED | Excavate & Haul T/W B/E | 13 | 21AUG98 | 10SEP98 | 0 02 | | DDB/E | █ Excavate & Haul T/W B/E | | | | | | | | | | | | | | | | | | |
| DDPE | Electrical Conduits T/W B/E | 10 | 31AUG98 | 16SEP98 | 19 02 | | DDB/E | △ Electrical Conduits T/W B/E | | | | | | | | | | | | | | | | | | |
| DDNE | Lime T/W B/E | 6 | 08SEP98 | 16SEP98 | 0 02 | | DDB/E | █ Lime T/W B/E | | | | | | | | | | | | | | | | | | |
| DDNF | Crushed Aggr. Base Course T/W B/E | 8 | 16SEP98 | 29SEP98 | 0 02 | | DDB/E | █ Crushed Aggr. Base Course T/W B/E | | | | | | | | | | | | | | | | | | |
| DDQE | LAY SURF T/W B ASPH ACCESS PH 2(3 EA) | 1 | 01OCT98 | 01OCT98 | 13 02 | | DDB/E | △ LAY SURF T/W B ASPH ACCESS PH 2(3 EA) | | | | | | | | | | | | | | | | | | |
| DDQF | Concrete Paving T/W B/E | 14 | 01OCT98 | 27OCT98 | 0 02 | | DDB/E | █ Concrete Paving T/W B/E | | | | | | | | | | | | | | | | | | |
| DDVE | Electrical Lighting Signals T/W B/E | 5 | 07OCT98 | 16OCT98 | 10 02 | | DDB/E | △ Electrical Lighting Signals T/W B/E | | | | | | | | | | | | | | | | | | |
| DDTF | REDRESS AFTER CONC PAV Ph 2 T/W B/E | 2 | 28OCT98 | 29OCT98 | 0 02 | | DDB/E | REDRESS AFTER CONC PAV Ph 2 T/W B/E █ | | | | | | | | | | | | | | | | | | |
| DDUE | Markings T/W B/E | 4 | 28OCT98 | 02NOV98 | 0 02 | | DDB/E | █ Markings T/W B/E | | | | | | | | | | | | | | | | | | |
| DDWA | Seeding/Grass Entire Job | 2 | 30OCT98 | 02NOV98 | 1 02 | | DDALL | △ Seeding/Grass Entire Job | | | | | | | | | | | | | | | | | | |
| DDUA | PERM PAVT MARKINGS | 3 | 30OCT98 | 03NOV98 | 0 02 | | DDALL | █ PERM PAVT MARKINGS | | | | | | | | | | | | | | | | | | |
| DDBC | Rmv Detour @ 225+00 T/W B/E | 1 | 03NOV98 | 03NOV98 | 0 02 | | DDB/F | █ Rmv Detour @ 225+00 T/W B/E | | | | | | | | | | | | | | | | | | |
| MILE4 | End of Phase 2 | 0 | | 03NOV98 | 0 02 | | DDB/E | ◆ End of Phase 2 | | | | | | | | | | | | | | | | | | |

ZZ OVERHEAD

| | | | | | | | | | | | | | | | | | | | | | | | | | | |
|------|----------|-----|---------|---------|------|--|-------|------------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
| DDZZ | Overhead | 140 | 02MAR98 | 02NOV98 | 1 22 | | DDALL | █ Overhead | | | | | | | | | | | | | | | | | | |
|------|----------|-----|---------|---------|------|--|-------|------------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|

| | | | |
|----------------|---------|---|-------------------|
| Project Start | 02MAR98 | █ | Early Bar |
| Project Finish | 03NOV98 | █ | Progress Bar |
| Data Date | 02MAR98 | █ | Critical Activity |
| Run Date | 01MAY98 | | |

H.B. ZACHRY COMPANY
ADDISON AIRPORT TAXIWAY
Work Package

Sheet 2 of 2
